

#	Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Remaining Duration	Start	Finish	Activity % Complete	Total Float	Variance - BL Project Finish	2015												2016												2017											
												Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	<b>Contract No. EP/SP/61/10 - The Design &amp; Construction Works</b>																																														
2	<b>LETTER OF ACCEPTANCE</b>																																														
3																																															
4																																															
5																																															
6	KD100200	LETTER OF ACCEPTANCE	1d	19-Nov-14	19-Nov-14	0d	19-Nov-14	19-Nov-14	100%		0d	LETTER OF ACCEPTANCE																																			
7	<b>MAJOR MILESTONES</b>																																														
8	<b>MC1 Milestones for Preliminaries and General Requirements</b>																																														
9																																															
10																																															
11	MC110100	MC1.1 - Substantial Completion of ER & IC Accommodation	0d	17-Dec-14	16-Dec-15	293d	16-Jan-15 A	16-Sep-17	100%	21d	-150d	MC1.1 - Substantial Completion of ER & IC Accommodation																																			
12	MC110200	MC1.2 - Joint signing of IC Agreement	0d	17-Dec-14	16-Dec-15	0d	16-Jan-15 A	11-Nov-15 A	100%		-19d	MC1.2 - Joint signing of IC Agreement																																			
13	MC110300	MC1.3 - Employer's consent granted on draft Contractor's Plans	0d	17-Dec-14	16-Dec-15	0d	16-Jan-15 A	11-Nov-15 A	100%		25d	MC1.3 - Employer's consent granted on draft Contractor's Plans																																			
14	<b>MC2 Milestones for Design of the Works</b>																																														
15	<b>MC2.1 The Employer's consent granted on Detailed Design Submission</b>																																														
16																																															
17	MC210100	MC2.1.1 - Employer's consent granted in respect of Detailed Design of Waste Receiving & Pre-treatment System	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-181d	MC2.1.1 - Employer's consent granted in respect of Detailed Design of Waste Receiving & Pre-treatment System																																			
18	MC210200	MC2.1.2 - Employer's consent granted in respect of Detailed Design of Anaerobic Digestion Treatment System	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-62d	MC2.1.2 - Employer's consent granted in respect of Detailed Design of Anaerobic Digestion Treatment System																																			
19	MC210300	MC2.1.3 - Employer's consent granted in respect of Detailed Design of Biogas treatment & CHP Generation System	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-209d	MC2.1.3 - Employer's consent granted in respect of Detailed Design of Biogas treatment & CHP Generation System																																			
20	MC210400	MC2.1.4 - Employer's consent granted in respect of Detailed Design of Composting System	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-30d	MC2.1.4 - Employer's consent granted in respect of Detailed Design of Composting System																																			
21	MC210500	MC2.1.5 - Employer's consent granted in respect of Detailed Design of CAPCS & WWTS	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-35d	MC2.1.5 - Employer's consent granted in respect of Detailed Design of CAPCS & WWTS																																			
22	MC210600	MC2.1.6 - Employer's consent granted in respect of Detail Design of control & instrumentation works	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	0%	-87d	-394d	MC2.1.6 - Employer's consent granted in respect of Detail Design of control & instrumentation works																																			
23	MC210700	MC2.1.7 - Employer's consent granted in respect of building services & electrical works	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	0%	-104d	-358d	MC2.1.7 - Employer's consent granted in respect of building services & electrical works																																			
24	MC210800	MC2.1.8 - Employer's consent granted in respect of Detailed Design of civil, structural & geotechnical works	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	0%	5d	-211d	MC2.1.8 - Employer's consent granted in respect of Detailed Design of civil, structural & geotechnical works																																			
25	MC210900	MC2.1.9 - Employer's consent granted in respect of Detailed Design of architectural & landscape works	0d	20-Jul-15	23-Feb-16	57d	28-Oct-15 A	17-Nov-16	100%		-258d	MC2.1.9 - Employer's consent granted in respect of Detailed Design of architectural & landscape works																																			
26	<b>MC2.2 Completion of the Design of the Works</b>																																														
27																																															
28	MC220100	MC2.2 - Completion of the Design of the Works	0d	23-Feb-16	23-Feb-16	0d	17-Nov-16	17-Nov-16	0%	-52d	-268d	MC2.2 - Completion of the Design of the Works																																			
29	<b>MC3 Milestones for Construction of the Works</b>																																														
30	<b>MC3.1 Construction of Civil and Structural Works</b>																																														
31																																															
32	MC310100	MC3.1.1 - Completion of site formation	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	100%	21d	-150d	MC3.1.1 - Completion of site formation																																			
33	MC310200	MC3.1.2 - Completion of 50% of piling works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	100%		-14d	MC3.1.2 - Completion of 50% of piling works																																			
34	MC310300	MC3.1.3 - Completion of 100% of piling works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	100%		0d	MC3.1.3 - Completion of 100% of piling works																																			
35	MC310400	MC3.1.4 - Completion of 50% of superstructure works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	100%		-56d	MC3.1.4 - Completion of 50% of superstructure works																																			
36	MC310500	MC3.1.5 - Completion of 80% of superstructure works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	100%		-151d	MC3.1.5 - Completion of 80% of superstructure works																																			
37	MC310600	MC3.1.6 - Completion of 100% of superstructure works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	0%	-67d	-217d	MC3.1.6 - Completion of 100% of superstructure works																																			
38	MC310700	MC3.1.7 - Completion of 100% of drainage, road and geotechnical works	0d	06-Jul-15	16-Mar-17	293d	22-Jul-15 A	16-Sep-17	0%	-67d	-147d	MC3.1.7 - Completion of 100% of drainage, road and geotechnical works																																			
39	<b>MC3.2 Delivery of Materials and Equipment to the Site</b>																																														
40																																															
41	MC320100	MC3.2.1 - Completion of Delivery of Pre-treatment System	125d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	0%	194d	-230d	MC3.2.1 - Completion of Delivery of Pre-treatment System																																			
42	MC320200	MC3.2.2 - Completion of Delivery of Anaerobic Digesters	0d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	0%	-46d	-142d	MC3.2.2 - Completion of Delivery of Anaerobic Digesters																																			
43	MC320300	MC3.2.3 - Completion of Delivery of Combined Heat and Power Units	0d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	100%		-6d	MC3.2.3 - Completion of Delivery of Combined Heat and Power Units																																			
44	MC320400	MC3.2.4 - Completion of Delivery of Composting Tunnels	0d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	0%	211d	-134d	MC3.2.4 - Completion of Delivery of Composting Tunnels																																			
45	MC320500	MC3.2.5 - Completion of Delivery of Centralized Air Pollution Control System	0d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	0%	-70d	-204d	MC3.2.5 - Completion of Delivery of Centralized Air Pollution Control System																																			
46	MC320600	MC3.2.6 - Completion of Delivery of Wastewater Treatment System	0d	26-Jan-16	02-Jul-16	82d	08-Jul-16 A	30-Dec-16	0%	-55d	-154d	MC3.2.6 - Completion of Delivery of Wastewater Treatment System																																			
47	<b>MC3.3 Equipment and System Installations</b>																																														
48																																															
49	MC330100	MC3.3.1 - Completion of Waste Receiving, Storage and Feeding System & Pre-treatment System	134d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-93d	-127d	MC3.3.1 - Completion of Waste Receiving, Storage and Feeding System & Pre-treatment System																																			
50	MC330200	MC3.3.2 - Completion of Anaerobic Digestion Treatment System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-98d	-112d	MC3.3.2 - Completion of Anaerobic Digestion Treatment System																																			
51	MC330300	MC3.3.3 - Completion of Biogas Cleaning and Storage System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-12d	-65d	MC3.3.3 - Completion of Biogas Cleaning and Storage System																																			
52	MC330400	MC3.3.4 - Completion of Heat Recovery and Power Generation System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-53d	-84d	MC3.3.4 - Completion of Heat Recovery and Power Generation System																																			
53	MC330500	MC3.3.5 - Completion of Composting System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-56d	-102d	MC3.3.5 - Completion of Composting System																																			
54	MC330600	MC3.3.6 - Completion of Centralized Air Pollution Control System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-75d	-143d	MC3.3.6 - Completion of Centralized Air Pollution Control System																																			
55	MC330700	MC3.3.7 - Completion of Wastewater Treatment System	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-80d	-175d	MC3.3.7 - Completion of Wastewater Treatment System																																			
56	MC330800	MC3.3.8 - Completion of control and instrumentation works	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-99d	-126d	MC3.3.8 - Completion of control and instrumentation works																																			
57	MC330900	MC3.3.9 - Completion of building services works & electrical works	0d	22-Jun-16	30-Nov-16	86d	20-Jan-17	11-May-17	0%	-103d	-178d	MC3.3.9 - Completion of building services works & electrical works																																			
58	<b>MC3.4 Architectural and Landscape works</b>																																														
59																																															











































#	Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Remaining Duration	Start	Finish	Activity % Complete	Total Float	Variance - BL Project Finish	2015												2016												2017											
												Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1132	<b>Digestate Dewatering System</b>																																														
1133	General																																														
1134			315d	12-Feb-15	25-May-16	71d	20-May-15 A	28-Nov-16		216d	-129d																																				
1135	PR170110	Issue orders & receive shop drawings from Digestate Dewatering suppliers	18d	12-Feb-15	11-Mar-15	22d	20-May-15 A	19-Sep-16	73.31%	265d	-377d																																				
1136	PR170165	Centrifuge	0d			0d	22-Jan-16 A	03-Aug-16 A	100%																																						
1137	PR170170	Centrate Tank	0d			59d	26-Aug-16*	18-Nov-16	0%	-58d																																					
1138	PR170171	Platform at Dewatering Area	0d			54d	09-Sep-16*	25-Nov-16	0%	-51d																																					
1139	PR170172	Bolffilter	0d			0d	05-Feb-16 A	16-Aug-16 A	100%																																						
1140	PR170173	Sandfilter	0d			31d	20-Jul-16 A	30-Sep-16	35%	37d																																					
1141	PR170174	Polymer Storage Tank	0d			51d	30-Jun-16 A	31-Oct-16	33%	-1d																																					
1142	PR170175	Centrate Discharge Pumps	0d			71d	21-Mar-16 A	28-Nov-16	68%	186d																																					
1143	PR170176	Polymer Feed Pumps	0d			0d	30-Jun-16 A	19-Jul-16 A	100%																																						
1144	PR170177	Break Tank	0d			59d	26-Aug-16*	18-Nov-16	0%	3d																																					
1145	PR170180	Polymer Dosing System	143d	27-Oct-15	25-May-16	51d	30-Jun-16 A	31-Oct-16	28%	92d	-109d																																				
1146	PR170210	Sieve Fine Plastic	0d			64d	26-May-16 A	17-Nov-16	65%	16d																																					
1147	PR170230	Anti-Foaming and Anti-Scalant Station	0d			51d	30-Jun-16 A	31-Oct-16	30%	29d																																					
1148	PR170250	Monorail (Dewatering)	0d			21d	11-Jul-16 A	15-Sep-16	0%	34d																																					
1149	<b>Composting System (Composting Tunnel, Maturation Area and Structurant Reception Area)</b>																																														
1150	General																																														
1151			315d	12-Feb-15	25-May-16	76d	30-Nov-15 A	05-Dec-16		211d	-134d																																				
1152	PR170100	Issue orders & receive shop drawings from Composting suppliers	18d	12-Feb-15	11-Mar-15	41d	30-Nov-15 A	17-Oct-16	60%	246d	-396d																																				
1153	PR170115	Star Screen Unit	0d			21d	18-May-16 A	15-Sep-16	70%	57d																																					
1154	PR170140	Mixing Unit	143d	09-Sep-15	11-Apr-16	65d	20-May-16 A	18-Nov-16	45%	13d	-154d																																				
1155	PR170190	Leachate Treatment, Pump & Sump Pump	143d	27-Oct-15	25-May-16	49d	21-Mar-16 A	27-Oct-16	65%	-11d	-107d																																				
1156	PR170200	Compost Bagging Machine	103d	09-Sep-15	05-Feb-16	65d	02-Sep-16*	05-Dec-16	0%	206d	-205d																																				
1157	PR170220	High Pressure Fans	103d	09-Sep-15	05-Feb-16	12d	18-Apr-16 A	02-Sep-16	92%	39d	-141d																																				
1158	PR170240	Heat Exchangers	103d	09-Sep-15	05-Feb-16	70d	05-Apr-16 A	25-Nov-16	66%	-19d	-199d																																				
1159	PR170260	Hot Water Circulation Pumps	103d	09-Sep-15	05-Feb-16	22d	13-Jun-16 A	19-Sep-16	78%	29d	-151d																																				
1160	PR170280	Tunnel Doors	103d	09-Sep-15	05-Feb-16	62d	02-Sep-16*	30-Nov-16	0%	-20d	-202d																																				
1161	PR170300	Tunnel Tiles	0d			11d	23-Mar-16 A	01-Sep-16	95%	4d																																					
1162	PR170320	Wheel Loader	0d			0d	23-Mar-16 A	11-Aug-16 A	100%																																						
1163	<b>Wastewater Treatment System (WWTS)</b>																																														
1164	General																																														
1165			266d	16-Mar-15	13-Apr-16	67d	08-Jul-15 A	22-Nov-16		220d	-154d																																				
1166	PR150100	Issue orders & receive shop drawings from WWTS suppliers	17d	16-Mar-15	10-Apr-15	4d	08-Jul-15 A	23-Aug-16	98%	283d	-340d																																				
1167	PR150120	Wastewater Treatment Plant (General)	103d	24-Sep-15	25-Feb-16	8d	11-Dec-15 A	29-Aug-16	90%	-56d	-126d																																				
1168	PR150130	Wastewater Treatment Plant (Chemical Dosing System)	0d			43d	22-Sep-16*	22-Nov-16	0%	-77d																																					
1169	PR150140	Ammonia Stripping Plant	134d	24-Sep-15	13-Apr-16	0d	24-Dec-15 A	15-Aug-16 A	100%		-85d																																				
1170	PR150160	Primary Sedimentation Tank (Conical Tank) and GRP Tank	0d			29d	17-Jun-16 A	28-Sep-16	13%	-39d																																					
1171	PR150180	SBR Submersible Mixer	0d			5d	13-Feb-16 A	24-Aug-16	98%	-18d																																					
1172	PR150200	Air Blowers	0d			39d	16-Aug-16 A	13-Oct-16	1%	-52d																																					
1173	PR150220	Air Compressor	0d			40d	23-Jun-16 A	14-Oct-16	48%	-53d																																					
1174	PR150240	ASP Stack (Insulation and Platform)	0d			45d	09-Sep-16*	14-Nov-16	0%	-53d																																					
1175	<b>Centralized Air Pollution Control (CAPC) System</b>																																														
1176	General																																														
1177			236d	12-Feb-15	26-Jan-16	67d	30-May-15 A	22-Nov-16		220d	-204d																																				
1178	PR180100	Issue orders & receive shop drawings from CAPC suppliers	18d	12-Feb-15	11-Mar-15	6d	30-May-15 A	25-Aug-16	92.04%	281d	-361d																																				
1179	PR180120	CAPC System Equipment (General)	103d	28-Aug-15	26-Jan-16	18d	14-Jan-16 A	12-Sep-16	90%	-37d	-155d																																				
1180	PR180140	GRP Tanks	0d			51d	31-Aug-16*	11-Nov-16	0%	-63d																																					
1181	PR180150	GRP Ductworks (Batch 1)	0d			8d	04-Jun-16 A	29-Aug-16	85%	-11d																																					
1182	PR180152	GRP Ductworks (Batch 2)	0d			28d	24-Jun-16 A	27-Sep-16	55%	-31d																																					
1183	PR180154	GRP Ductworks (Batch 3)	0d			43d	22-Sep-16*	22-Nov-16	0%	-70d																																					
1184	PR180160	Venturi Scubber	0d			0d	14-Jan-16 A	21-Jul-16 A	100%																																						
1185	PR180180	Wet Scubber	0d			0d	14-Jan-16 A	21-Jul-16 A	100%																																						
1186	PR180200	Chemical Scubber	0d			6d	14-Jan-16 A	25-Aug-16	98%	-25d																																					
1187	PR180205	Pumps	0d			0d	14-Jan-16 A	05-May-16 A	100%																																						




















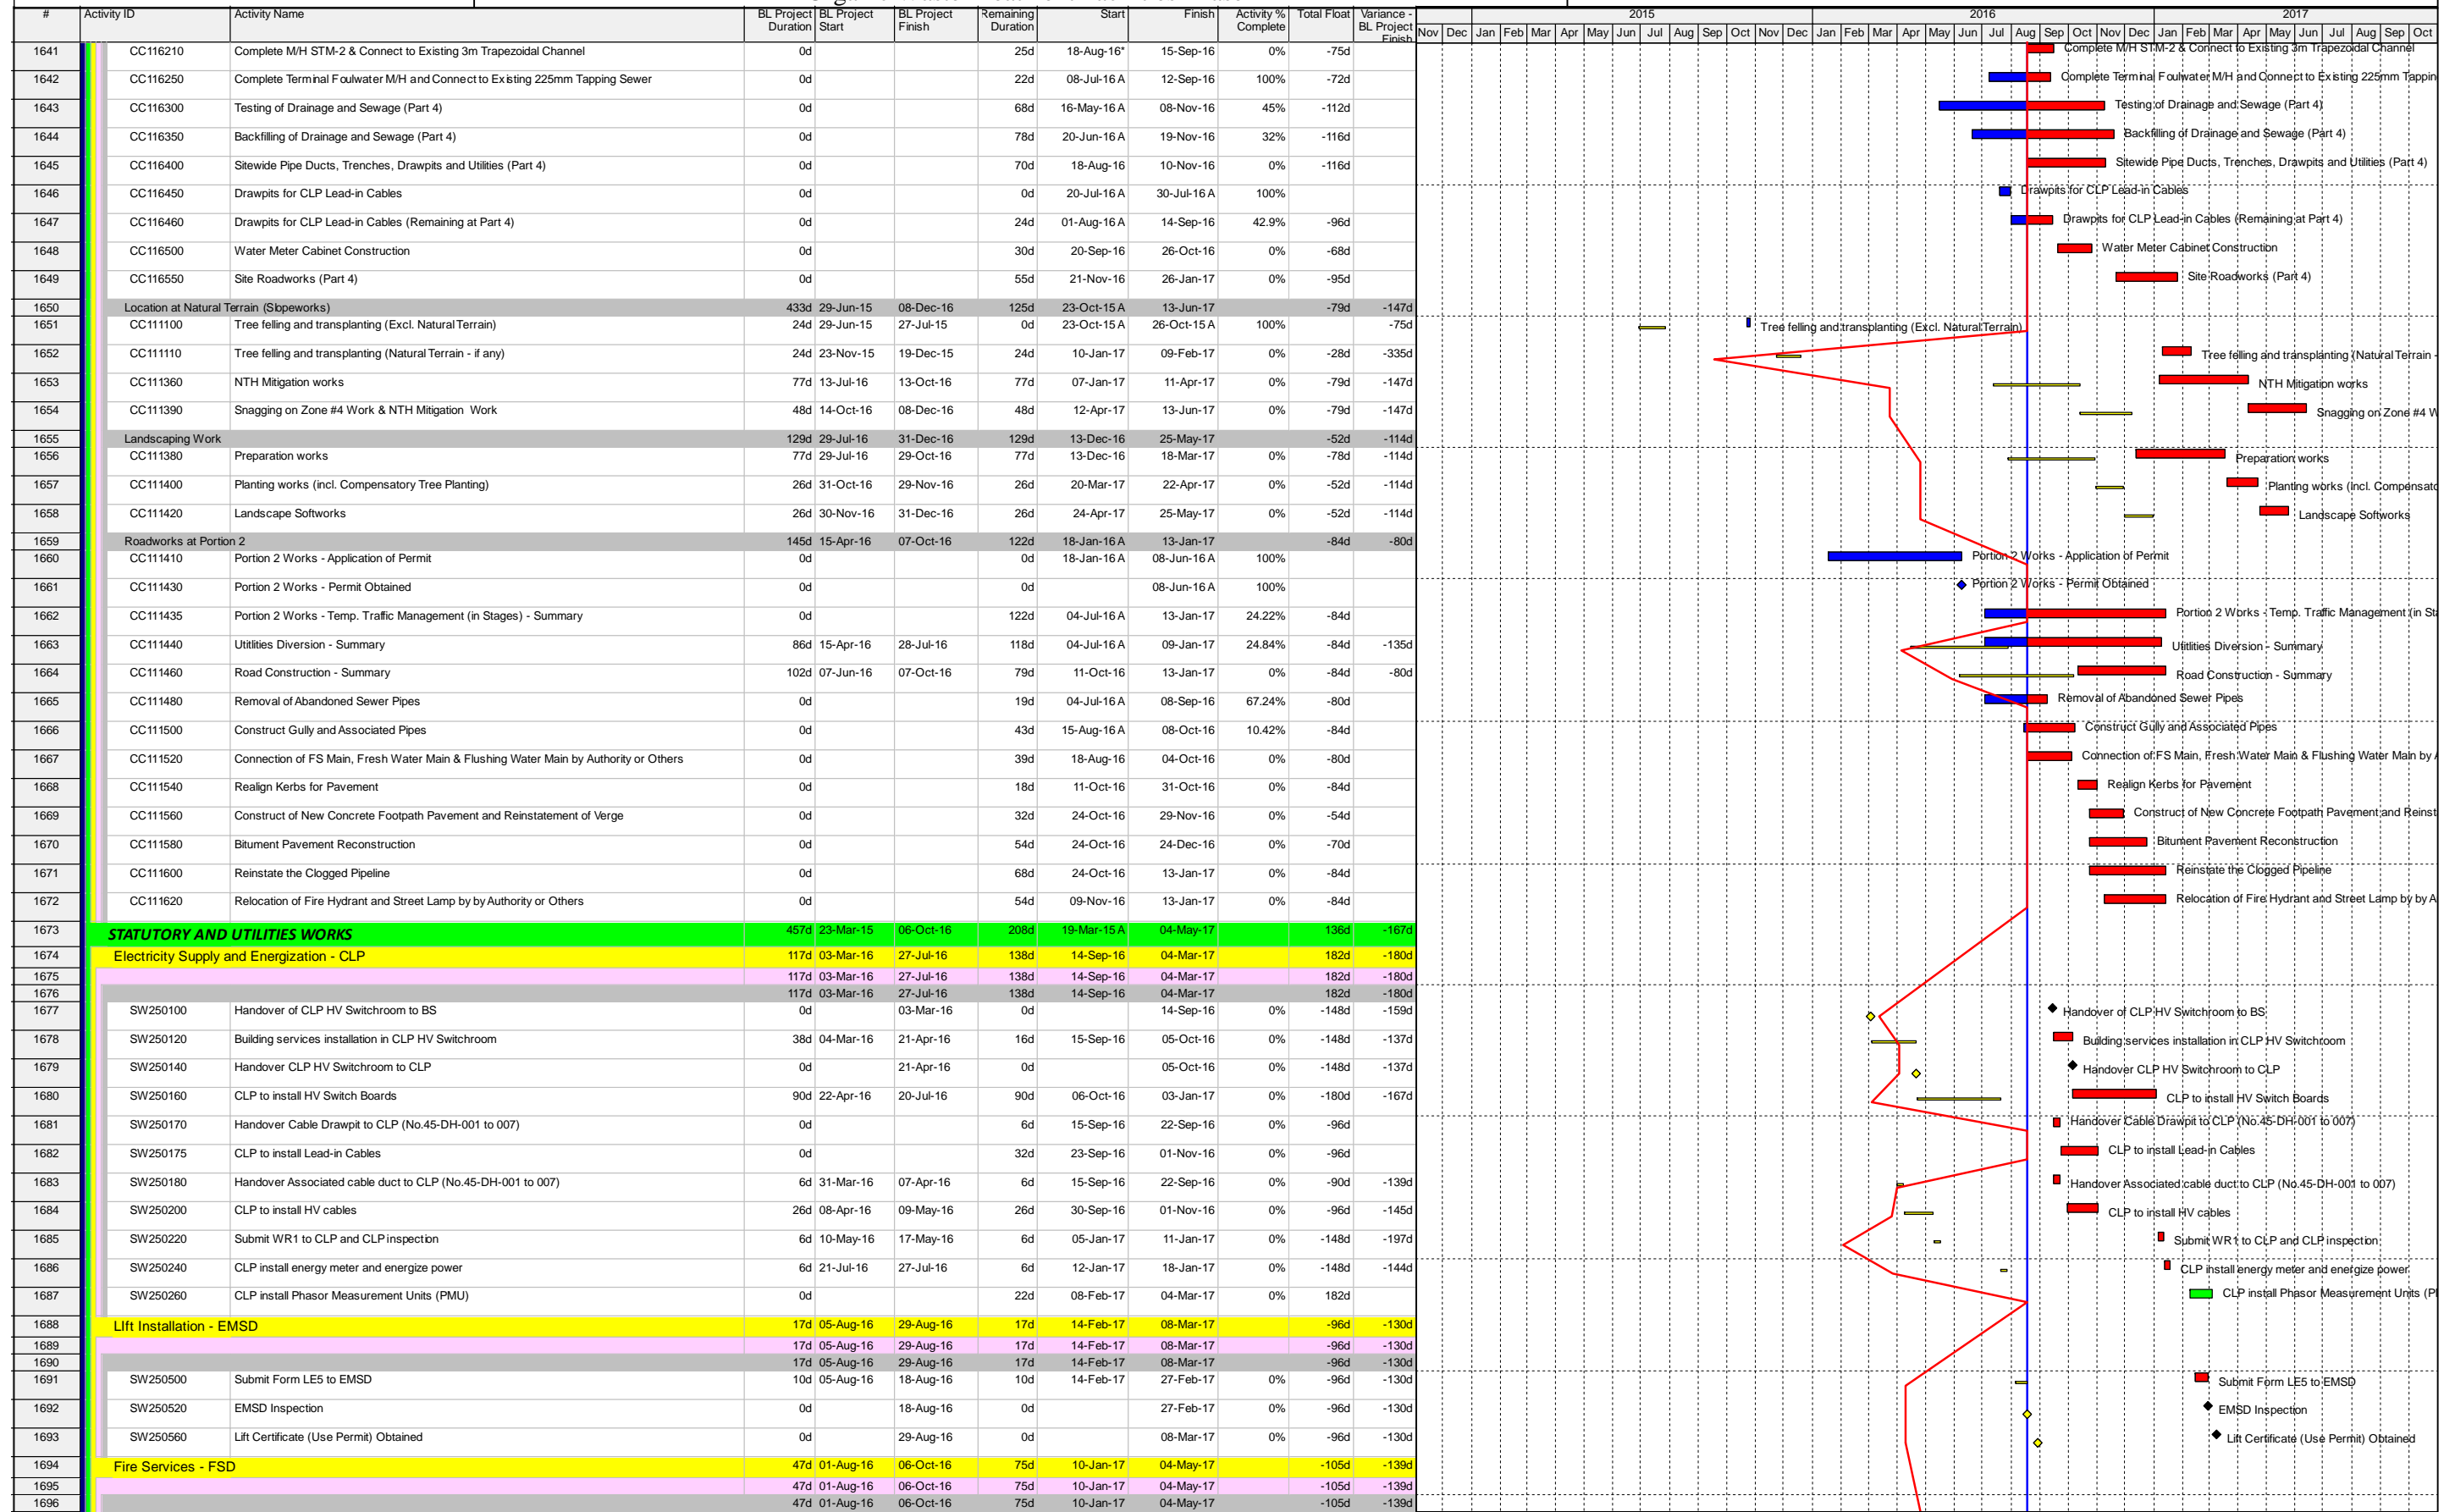











Environmental Protection Department of the HKSAR			Contract No. EP/SP/61/10 Organic Waste Treatment Facilities Phase 1										Contract Programme Progress Updated on 17-Aug-16 OSCAR BIOENERGY JV																																			
#	Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Remaining Duration	Start	Finish	Activity % Complete	Total Float	Variance - BL Project Finish	2015 Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec												2016 Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec												2017 Jan Feb Mar Apr May Jun Jul Aug Sep Oct												
1916	EM120220	Installation of Combine Heat Power System Accessories no. 1 to 3	0d			26d	01-Nov-16	30-Nov-16	0%	16d																										Installation of Combine Heat Power System Accessories no.												
1917	EM120250	Installation of Heat Recovery system / H2S Polishing (duplicated, to be deleted)	26d	18-Aug-16	17-Sep-16	26d	08-Dec-16	10-Jan-17	0%	-10d	-93d																									Installation of Heat Recovery system / H2S Polishing												
1918	EM120260	Installation of CHP Stack	0d			26d	08-Dec-16	10-Jan-17	0%	-79d																										Installation of CHP Stack												
1919	EM120320	Heat Recovery and Power Generation System Pipework	0d			78d	08-Dec-16	15-Mar-17	0%	-62d																										Heat Recovery and Power Generation S												
1920	EM120350	Installation of Continuous Emissions Monitoring System (CEMS)	26d	01-Nov-16	30-Nov-16	26d	08-Dec-16	10-Jan-17	0%	-31d	-32d																									Installation of Continuous Emissions Monitoring Syst												
1921	EM120400	Cable Tray Laying Works	26d	01-Nov-16	30-Nov-16	14d	13-Oct-16	28-Oct-16	0%	-12d	28d																									Cable Tray Laying Works												
1922	EM120410	Local Control Panel / Switch	0d			15d	29-Oct-16	15-Nov-16	0%	-12d																										Local Control Panel / Switch												
1923	EM120450	Cabling Works	39d	17-Oct-16	30-Nov-16	20d	08-Dec-16	03-Jan-17	0%	-31d	-26d																									Cabling Works												
1924	EM120500	Completion of E&M Installation of Heat Recovery and Power Generation System	0d			0d			15-Mar-17	0%	-62d	-84d																									Completion of E&M Installation of Heat R											
1925	Installation of Control Panels		0d			23d	31-Dec-16	27-Jan-17		-147d																																						
1926	Installation of Control Panels		0d			23d	31-Dec-16	27-Jan-17		-147d																																						
1927	EM19021H	Installation of Panels at Heat Recovery & CHP MCC Rooms	0d			23d	31-Dec-16	27-Jan-17	0%	-147d																										Installation of Panels at Heat Recovery & CHP M												
1928	Biogas Cleaning and Storage System		108d	02-Jul-16	08-Nov-16	105d	12-Sep-16	18-Jan-17		-16d	-58d																																					
1929	Biogas Cleaning and Storage System		108d	02-Jul-16	08-Nov-16	105d	12-Sep-16	18-Jan-17		-16d	-58d																																					
1930	Biogas Cleaning and Storage System		108d	02-Jul-16	08-Nov-16	105d	12-Sep-16	18-Jan-17		-16d	-58d																																					
1931	EM130100	Installation of Bio Gas Cleaning System no.1 (Desulphurisation)	26d	02-Jul-16	01-Aug-16	40d	12-Sep-16	31-Oct-16	0%	-34d	-75d																									Installation of Bio Gas Cleaning System no.1 (Desulphurisation)												
1932	EM130150	Installation of Bio Gas Cleaning System no.2 (Desulphurisation)	26d	02-Aug-16	31-Aug-16	40d	12-Sep-16	31-Oct-16	0%	-26d	-49d																									Installation of Bio Gas Cleaning System no.2 (Desulphurisation)												
1933	EM130200	Installation of Bio Gas Storage Tank	26d	01-Sep-16	03-Oct-16	18d	06-Dec-16	28-Dec-16	0%	-96d	-71d																									Installation of Bio Gas Storage Tank												
1934	EM130350	Biogas Cleaning and Storage System Pipework	31d	15-Sep-16	24-Oct-16	43d	17-Nov-16	09-Jan-17	0%	-88d	-63d																									Biogas Cleaning and Storage System Pipework												
1935	EM130400	Cable Tray Laying Works	39d	01-Sep-16	19-Oct-16	60d	11-Oct-16	19-Dec-16	0%	-9d	-52d																									Cable Tray Laying Works												
1936	EM130410	Local Control Panel / Switch	0d			25d	16-Nov-16	14-Dec-16	0%	-9d																										Local Control Panel / Switch												
1937	EM130450	Cabling Works	17d	20-Oct-16	08-Nov-16	45d	24-Nov-16	18-Jan-17	0%	-16d	-58d																									Cabling Works												
1938	EM130500	Completion of E&M Installation of Biogas Cleaning and Storage System	0d			0d			18-Jan-17	0%	-16d	-58d																									Completion of E&M Installation of Biogas Cleaning											
1939	Biogas Distribution System		74d	02-Jul-16	27-Sep-16	114d	10-Sep-16	27-Jan-17		-43d	-100d																																					
1940	Biogas Distribution System		74d	02-Jul-16	27-Sep-16	113d	10-Sep-16	26-Jan-17		-42d	-99d																																					
1941	Biogas Distribution System		74d	02-Jul-16	27-Sep-16	113d	10-Sep-16	26-Jan-17		-42d	-99d																																					
1942	EM130250	Installation of Standby Flaring Gas Unit	18d	02-Jul-16	22-Jul-16	12d	10-Sep-16	24-Sep-16	0%	-74d	-54d																									Installation of Standby Flaring Gas Unit												
1943	EM130260	Installation of Biogas Blowers	18d	02-Jul-16	22-Jul-16	42d	10-Sep-16	01-Nov-16	0%	-74d	-84d																									Installation of Biogas Blowers												
1944	EM130270	Installation of Biogas Cooling and Condensate Removal System	18d	02-Jul-16	22-Jul-16	42d	21-Sep-16	10-Nov-16	0%	-82d	-92d																									Installation of Biogas Cooling and Condensate Removal System												
1945	EM130272	Installation of Racks and Supports (Biogas Area)	0d			30d	22-Oct-16	25-Nov-16	0%	-81d																										Installation of Racks and Supports (Biogas Area)												
1946	EM130275	Biogas Distribution System Pipework	0d			50d	26-Nov-16	26-Jan-17	0%	-42d																										Biogas Distribution System Pipework												
1947	EM130278	Carbon Filters	0d			20d	10-Sep-16	05-Oct-16	0%	51d																										Carbon Filters												
1948	EM130280	Cable Tray Laying Works	39d	23-Jul-16	06-Sep-16	30d	26-Nov-16	03-Jan-17	0%	-33d	-96d																									Cable Tray Laying Works												
1949	EM130285	Local Control Panel / Switch	0d			15d	09-Dec-16	28-Dec-16	0%	-33d																										Local Control Panel / Switch												
1950	EM130290	Cabling Works	17d	07-Sep-16	27-Sep-16	30d	09-Dec-16	16-Jan-17	0%	-33d	-90d																									Cabling Works												
1951	EM130295	Completion of E&M Installation of Biogas Disgtribution System	0d			0d			26-Jan-17	0%	-42d	-99d																									Completion of E&M Installation of Biogas Disgtrib											
1952	Installation of Control Panels		0d			23d	31-Dec-16	27-Jan-17		-147d																																						
1953	Installation of Control Panels		0d			23d	31-Dec-16	27-Jan-17		-147d																																						
1954	EM19021G	Installation of Panels at Biogas MCC Rooms	0d			23d	31-Dec-16	27-Jan-17	0%	-147d																										Installation of Panels at Biogas MCC Rooms												
1955	Wastewater Treatment System		110d	04-Feb-16	22-Jun-16	109d	09-Sep-16	20-Jan-17		-100d	-175d																																					
1956	Wastewater Treatment System		94d	26-Feb-16	22-Jun-16	109d	09-Sep-16	20-Jan-17		-100d	-175d																																					
1957	Wastewater Treatment System		94d	26-Feb-16	22-Jun-16	109d	09-Sep-16	20-Jan-17		-100d	-175d																																					
1958	EM140100	Installation of Pumping System and associated pipework	40d	26-Feb-16	16-Apr-16	40d	27-Sep-16	14-Nov-16	0%	-91d	-174d																									Installation of Pumping System and associated pipework												
1959	EM140150	Installation of Aeration System	24d	18-Apr-16	17-May-16	24d	15-Nov-16	12-Dec-16	0%	-88d	-174d																									Installation of Aeration System												
1960	EM140200	Installation of Odour Containment System (GRP Cover for WWTP)	26d	18-May-16	17-Jun-16	15d	28-Dec-16	14-Jan-17	0%	-99d	-174d																									Installation of Odour Containment System (GRP Co												
1961	EM140250	Installation of Odour Extraction Ductwork (for WWTP)	21d	28-May-16	22-Jun-16	21d	23-Dec-16	19-Jan-17	0%	-99d	-174d																									Installation of Odour Extraction Ductwork (for WW												
1962	EM140300	Installation of Ammonia Stripping Plant	51d	14-Apr-16	15-Jun-16	82d	09-Sep-16	16-Dec-16	0%	-103d	-154d																									Installation of Ammonia Stripping Plant												
1963	EM140330	Wastewater Treatment System Pipework	0d			74d	17-Oct-16	13-Jan-17	0%	-100d																										Wastewater Treatment System Pipework												
1964	EM140335	Chemical Storage & Dosing System	0d			40d	02-Dec-16	20-Jan-17	0%	-100d																										Chemical Storage & Dosing System												
1965	EM140340	Primary Sedimentation Tank (Conical Tank)	0d			20d	16-Nov-16	08-Dec-16	0%	-66d																										Primary Sedimentation Tank (Conical Tank)												
1966	EM140345	Installation of ASP Stack	0d			18d	17-Dec-16	10-Jan-17	0%	-91d																										Installation of ASP Stack												
1967	EM140350	Cable Tray Laying Works	21d	18-Apr-16	12-May-16	60d	13-Oct-16	21-Dec-16	0%	-89d	-185d																									Cable Tray Laying Works												
1968	EM140360	Local Control Panel / Switch	0d			28d	19-Nov-16	21-Dec-16	0%	-89d																										Local Control Panel / Switch												
1969	EM140400	Cabling Works	26d	13-May-16	14-Jun-16	40d	19-Nov-16	07-Jan-17	0%	-89d	-171d																									Cabling Works												
1970	EM140450	Completion of E&M Installation of Wastewater Treatment System	0d			0d			20-Jan-17	0%	-100d	-175d																									Completion of E&M Installation of Wastewater Tre											
1971	Installation of Control Panels		41d	04-Feb-16	29-Mar-16	36d	25-Oct-16	05-Dec-16		-100d	-207d																																					
1972	Installation of Control Panels		41d	04-Feb-16	29-Mar-16	36d	25-Oct-16	05-Dec-16		-100d	-207d																																					



Main data table with columns for Activity ID, Activity Name, BL Project Duration, BL Project Start, BL Project Finish, Remaining Duration, Start, Finish, Activity % Complete, Total Float, Variance - BL Project Finish, and monthly progress bars for 2015, 2016, and 2017.

Project: v1.4\_up\_17Aug16  
Ref.: WS-OSC-00-0-TM-0061-A, Date: 27-Aug-2016

Legend for chart symbols: Primary Baseline (green), Activity (orange), Critical (red), Actual Milestone (diamond), Baseline Milestone (diamond), Milestone (diamond), Actual Work (blue).





